

SELECTED PROJECT EVIDENCE

SM Iloilo Terminal Market

Masonry Quantity Take-Off, Cost Proposal and Drawing Review

Client

SM Prime Corporation

Location

Mandurriao, Iloilo City

Completed

2025

Role

Masonry works / quantity surveying support



01 / COST PROPOSAL

Commercial scope at a glance

PROPOSAL TOTAL	GENERAL REQUIREMENTS	ARCHITECTURAL FINISHES
P17.086M	P1.925M	P15.161M
Documented cost proposal	11.3% of proposal	88.7% of proposal

Trade / work package	Amount	Share
General requirements	P1,925,000.00	11.3%
Masonry works	P4,937,244.67	28.9%
Plastering	P4,105,816.77	24.0%
Rubbed concrete - ceiling	P1,977,819.00	11.6%
Rubbed concrete - beam	P1,598,400.00	9.4%
Rubbed concrete - column	P998,400.00	5.8%
Zocalo	P562,910.00	3.3%
Wet-stall countertop	P980,481.00	5.7%
TOTAL	P17,086,071.44	100.0%

02 / SELECTED BOQ EVIDENCE


Measured quantities and unit-rate extensions

Description	Unit	Quantity	Unit rate	Amount
CHB laying - Ground Floor	sq.m	1,482.64	P962.00	P1,426,299.68
CHB laying - Mezzanine	sq.m	1,433.55	P962.00	P1,379,076.03
CHB laying - Second Floor	sq.m	1,367.60	P962.00	P1,315,631.20
CHB laying - Roof Deck 4 in.	sq.m	848.48	P962.00	P816,237.76
Plastering - Ground Floor	sq.m	2,965.28	P400.00	P1,186,112.00
Plastering - Mezzanine	sq.m	2,867.10	P400.00	P1,146,840.00
Plastering - Second Floor	sq.m	2,735.20	P400.00	P1,094,080.00
Plastering - Roof Deck	sq.m	1,696.96	P400.00	P678,784.00
Zocalo - Mezzanine	l.m	242.50	P500.00	P121,250.00
Zocalo - Second Floor	l.m	671.20	P500.00	P335,600.00
Zocalo - Roof Deck	l.m	212.12	P500.00	P106,060.00
Wet-stall countertop rebar (OSM)	kg	8,200.00	P8.25	P67,650.00
Wet-stall countertop formwork	sq.m	666.30	P800.00	P533,040.00
Wet-stall countertop concreting	cu.m	99.95	P3,800.00	P379,810.00

03 / COMPLEX 2D DRAWING

Ground-floor wall-type coordination

Selected source-plan extract used to interpret masonry zones, wall classifications and measurement boundaries.

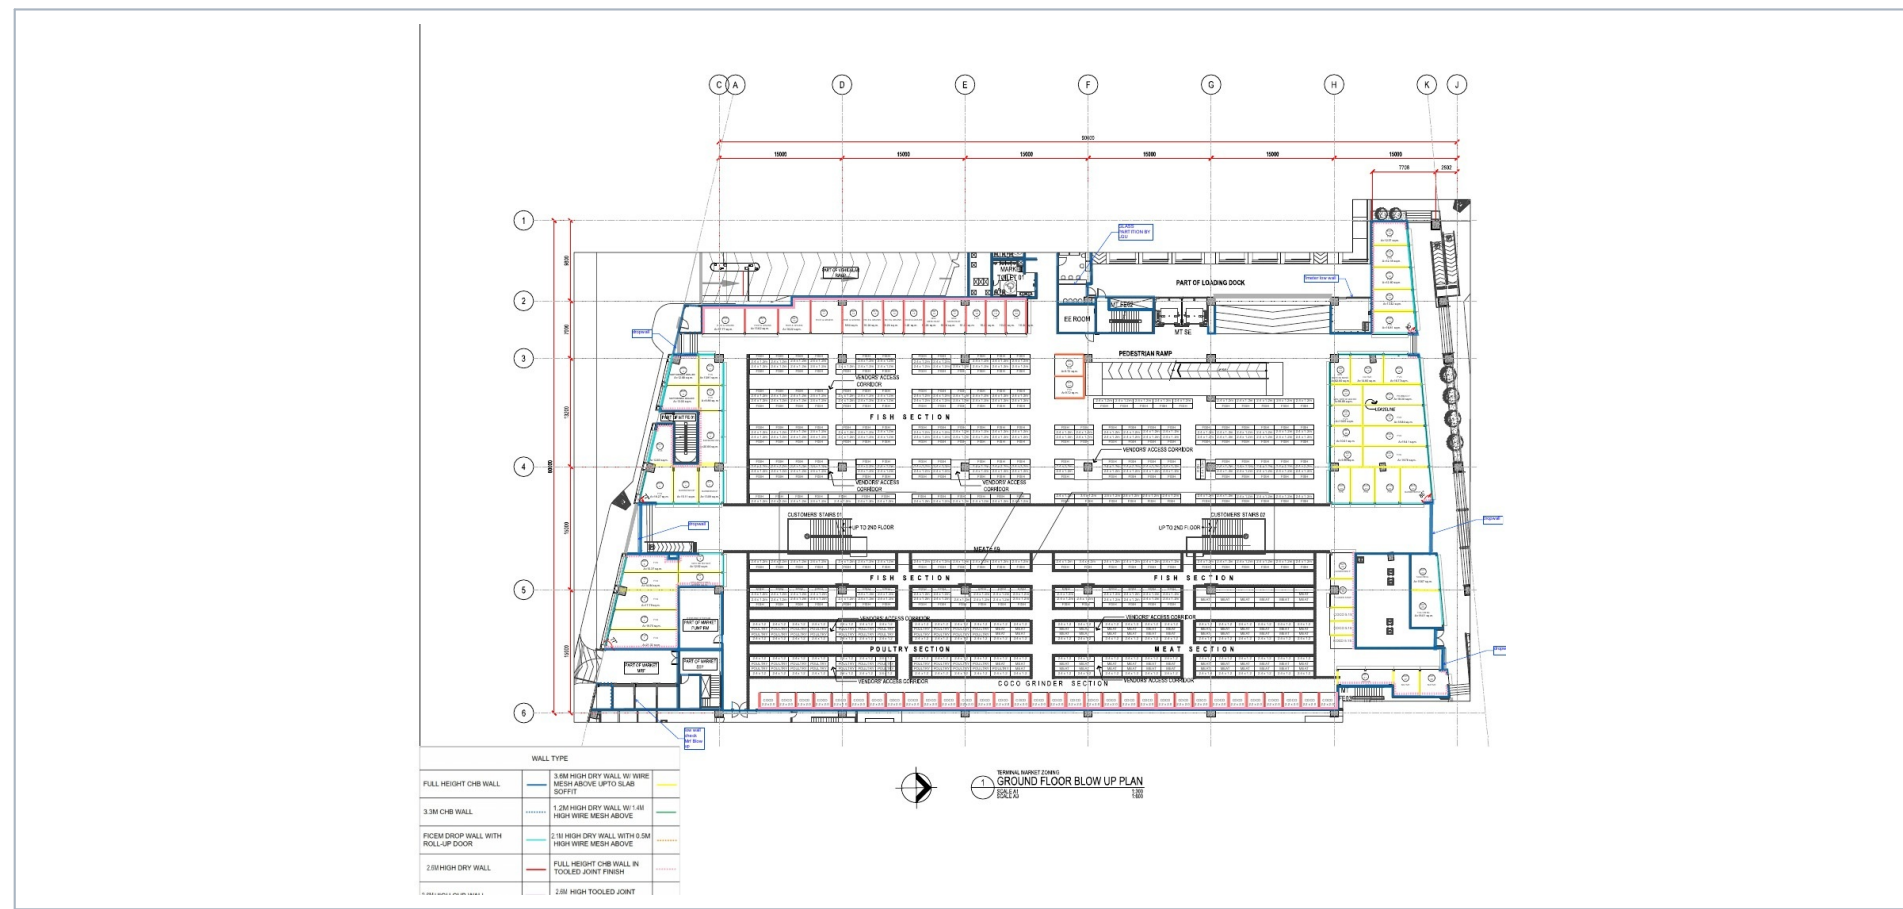

04 / COMPLEX 2D DRAWING

Second-floor wall-type coordination


A second-level plan demonstrates consistent trade measurement across a large, irregular market floor plate.



05 / SHOP AND DETAIL DRAWING

Market-stall detail coordination

Selected plan, reflected ceiling plan, elevations and sections used to understand construction interfaces and measurement requirements.

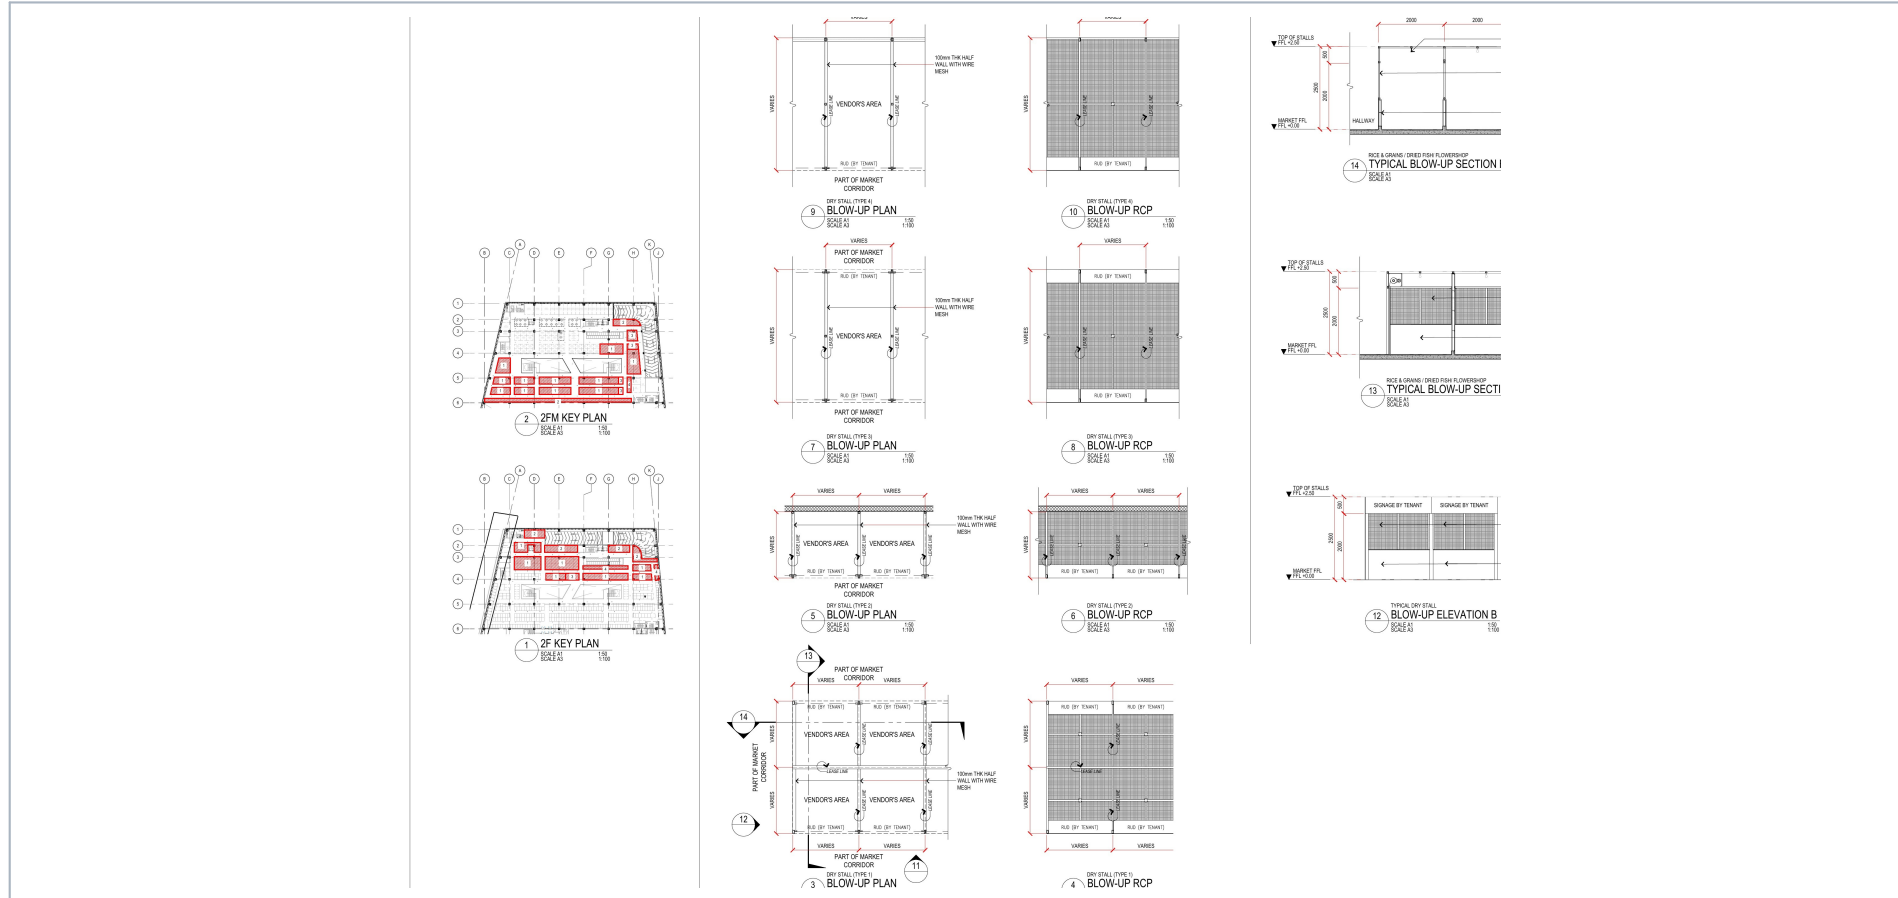

SUBJECT

Drop Signage Panels (BOQ Item E) — Panel Height, Framing Call-out, Paint Extent & Sheet Joints

PROJECT	Mail Redevelopment — Game Park Ceiling Works BOQ Item E: Bowling Lane Number Drop Signage (16 sets)	DATE ISSUED	20 Aug 2026
CLIENT	[REDACTED]	REPLY NEEDED BY	24 Aug 2026
TO / ATTN	Project Architect — [REDACTED]	DISCIPLINE	Architectural / Interiors
FROM	Engr. Mark Raphael Tive, Project Manager	PRIORITY	HIGH holds fabrication
LOCATION	[REDACTED] — Game Park Area	REFERENCE	Dwg. GP.ID.05, Detail BT-06; Architect's mark-up

BACKGROUND

BOQ Item E covers **16 panel sets** of lane number drop signage — Lanes 1–14 across Bowling Alleys 1 and 2, plus 2 sets at the Private Bowling Area. In reconciling our quantity take-off with the Architect's mark-up, four items can be read in more than one way. Please confirm the items below so that quantities, procurement and shop fabrication can be finalized.

QUERIES AND MRK BASIS

#	QUERY	CURRENT MRK BASIS (FOR CONFIRMATION)
1	Panel height. An earlier take-off used 2.33 m; Detail BT-06 shows a curved top that brings the overall height to 2.50 m. Please confirm the overall panel size for fabrication.	1.52 m W x 2.50 m H overall (full curved top). Sheet measured on the overall rectangle: 3.80 m ² x 16 sets = 60.80 m² .
2	Framing call-out "2x2 / 2x6" . The mark-up notation can be read as a tube section size or as a member-count multiplier. Please confirm the intended framing section and layout.	25 x 25 mm (1" x 1") tubular frame: 16.08 lm x 16 sets = 257.28 lm (46 lengths x 6.0 m, incl. 5% waste).
3	Paint extent. The mark-up and our take-off apply different painting multipliers (3-sided vs. 4-sided). Please confirm the surfaces to be painted and the finish system (primer, top coat, colour).	Paint all exposed surfaces; concealed faces primer only. Painted area to be re-measured on your reply.
4	Sheet joints. Each panel (1.52 x 2.50 m) is larger than a standard 1.22 x 2.44 m (4' x 8') perforated sheet in both directions, so sheets must be joined. Please confirm the joint location/method and whether perforations must line up across joints.	Butt joints on framing members (concealed), perforations aligned. 24 sheets (4' x 8') incl. 15% cutting waste.

IMPACT

COST IMPACT

POSSIBLE

Items 1–3 change the measured quantities under Item E. Revised amounts will follow your reply.

TIME IMPACT

POSSIBLE

Procurement (24 sheets, 46 tube lengths) and shop fabrication are released on your reply.

ATTACHMENTS

1. Marked-up extract — Dwg. GP.ID.05 / Detail BT-06 (1 p.)
2. Item E quantity memo — lm and m² build-up (1 p.)

PREPARED BY

Engr. Mark Raphael Tive

Project Manager · MRK Construction Corporation

SIGNATURE

DATE _____

20 Aug 2026

ARCHITECT'S RESPONSE

Does this reply change the Contract Sum or Time? ☐ No ☐ Yes — variation to follow

NAME / POSITION _____ SIGNATURE _____ DATE _____

SUBJECT

Material Substitution — 150 mm (6") CHB Toilet Wall Partitions in lieu of Phenolic Board Partitions

PROJECT	Additional 2nd Floor Toilet — Construction	DATE SUBMITTED	16 Sep 2026
CLIENT	██████████ PO No. ██████████	APPROVAL DUE	18 Sep 2026
TO / ATTN	Client Project Architect — ██████████	DRAWING REF.	Toilet layout & partition details
FROM	Engr. Mark Raphael Tive, Project Manager	LOCATION	CL 25/L, 2nd Floor, Bacolod City
SUBMITTAL TYPE	☒ Material substitution ☐ Shop drawing ☒ Product data ☐ Sample ☒ Method statement		

PROPOSAL

Build the toilet wall partitions in **150 mm (6") concrete hollow blocks (CHB)**, plastered and tiled, in lieu of the phenolic board partitions shown. This is a contractor-initiated substitution raised with the catch-up works for the 2F toilet.

ITEM	SPECIFIED — PHENOLIC BOARD	PROPOSED — 150 MM CHB
System	Phenolic compact board panels on the supplier's hardware	150 mm CHB, non-load-bearing; cement plaster both faces; wall tiles per finish schedule
Anchorage	Floor and wall brackets per supplier	10 mm Ø vertical bars @ 600 mm O.C.; horizontal bars every 3rd course dowels drilled and epoxy-anchored into the slab
Wet-area use	Moisture-resistant	Moisture- and impact-resistant; no hardware to maintain
Availability	Made to order — supplier lead time	Locally available; work can start at once

TECHNICAL NOTES

- **Added weight:** CHB is heavy than phenolic board. A load check of the existing 2F slab is attached for the Client's structural review.
- Top of wall laterally restrained at ceiling/slab level per the attached wall section.
- Waterproofing upturn on wet-area walls is placed before plaster and tiles, together with the floor waterproofing.

IMPACT

COST IMPACT NONE No added cost to the Client — contractor-initiated substitution.	TIME IMPACT SAVES TIME Work can start at once; supports the 25 Sep 2026 catch-up target.
---	--

ITEMS SUBMITTED

1. Partition layout and typical wall section (1 sheet)
2. CHB supplier data and compressive strength test certificate
3. Method statement — set-out, dowelling, block laying, plastering, curing
4. Load check — existing 2F slab (added partition weight)

CONTRACTOR'S CERTIFICATION

MRK has reviewed this submittal and certifies that it complies with the Contract Documents except for the deviation stated above.

SUBMITTED BY

Engr. Mark Raphael Tive

Project Manager · MRK Construction Corporation

SIGNATURE

DATE _____

16 Sep 2026

CLIENT / ARCHITECT'S ACTION

NAME / POSITION	SIGNATURE
DATE	

☐ Approved
 ☐ Approved as noted
 ☐ Revise & resubmit
 ☐ Rejected

SUBJECT

Revised Footing F2 — Increase to 2.00 m × 3.70 m (Dormitory Reclassification)

PROJECT	3-Storey + Roof Deck Building — Dormitory Reclassification	DATE ISSUED	04 Jun 2026
CLIENT		EFFECTIVE	Immediately
TO / ATTN	Site Foreman & Structural Crew —	REFERENCE	Revised Foundation Plan & Footing Schedule (Rev. 1)
FROM	Engr. Mark Raphael Tive, Project Manager	LOCATION	, Bacolod City
INSTRUCTION TYPE	☒ Change in work ☒ Quality / hold point ☐ Safety ☐ Schedule		


REASON

The structural re-evaluation for the dormitory reclassification (**NSCP 2015, Seismic Zone 4, SMRF**) revised footing F2 from the original design. All F2 footings shall be built to the revised size below.

INSTRUCTIONS

1. **HOLD all F2 locations** — no concreting on any F2 footing until this instruction is carried out and inspected.
2. Re-set out F2 to **2.00 m × 3.70 m** per the revised foundation plan, noting any offset from the column centre. Verify the set-out with the Project Engineer before excavating.
3. Excavate to the design bottom-of-footing level. The bottom must be firm, level and free of loose soil and standing water; place bedding per plan.
4. Place bars per the revised Footing Schedule (size and spacing, both directions). Keep **75 mm clear cover** to bottom and sides (cast against earth). Use concrete spacer blocks only — no stones or wood.
5. Set column dowels and ties per the Column Schedule; brace them so they cannot move during the pour.
6. **HOLD POINT:** call the Project Engineer for rebar inspection. No pour without a signed pour checklist.
7. Concrete per the structural general notes. Take cylinder samples for 28-day strength tests and cure for at least 7 days.
8. Mark the revision on the site drawing set and report actual quantities (excavation, concrete, rebar) to the QS for the cost record.

SKETCH — REVISED FOOTING F2

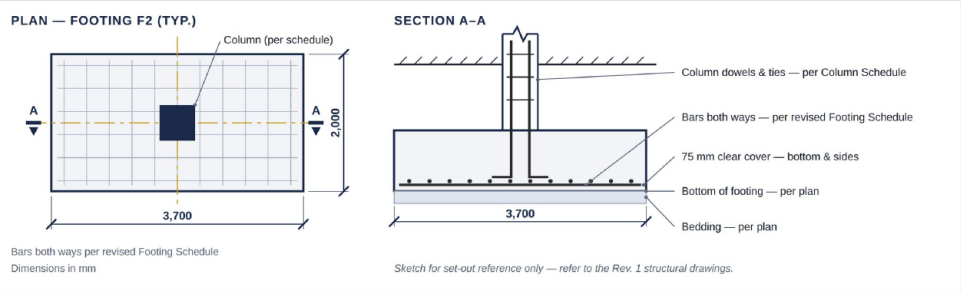

IMPACT

COST IMPACT Added excavation, concrete and rebar — quantified by the QS and recorded as a variation.	YES	TIME IMPACT Absorbed within foundation works; report any delay the same day.	MINOR
--	------------	--	--------------

ISSUED BY
Engr. Mark Raphael Tive
Project Manager · MRK Construction Corporation

SIGNATURE

DATE
04 Jun 2026

RECEIVED & UNDERSTOOD — SITE FOREMAN

REMARKS / SITE QUERIES

Copy to: Project Engineer · QS · Site file

NAME

SIGNATURE

DATE / TIME

SUBJECT

Dining Area Aircon — Revert from Wall-Mounted Inverter to Ceiling Cassette Units

PROJECT	Restaurant & Mini Mart Fit-Out	DATE ISSUED	18 Sep 2026
CLIENT	[REDACTED]	INSTRUCTION DATE	17 Sep 2026, site meeting
TO / ATTN	Owner — [REDACTED]	GIVEN BY	Owner — [REDACTED]
FROM	Engr. Mark Raphael Tive, Project Manager	CONTRACT REF.	Agreement 08 Sep 2026; approved BOQ note
CC	Site file · QS		

VERBAL INSTRUCTION RECEIVED

"Change the dining area air-conditioning back to ceiling cassette units, as in the original design, instead of the wall-mounted inverter units in the contract."

CONTRACT VS. INSTRUCTED

	CONTRACT (APPROVED BOQ)	AS INSTRUCTED
Unit type	Wall-mounted inverter split units — changed from ceiling cassette for budget, per approved BOQ note	Ceiling cassette units (original design)
Capacity	8.5 HP total — 2 × 3.0 HP + 1 × 2.5 HP	Same total capacity (to be confirmed)
Amount	₱248,000.00	₱405,000.00
Variance	—	+ ₱157,000.00 (indicative)

Amounts exclude ceiling openings and supports, and revised refrigerant and drain piping — to be quantified after site verification.

CONDITIONS

1. The change will be processed as **Change Order No. 1**. The **₱157,000.00** is indicative until site verification is complete.
2. Procurement of the dining area units is **on hold** until Change Order No. 1 is signed. All other works continue.
3. Any effect on the **15 Oct 2026 turnover** (unit lead time, ceiling rework) will be stated in Change Order No. 1.

Supporting records: site meeting notes (17 Sep 2026) · approved BOQ note — dining aircon · supplier quotation — ceiling cassette units.

IMPACT

COST IMPACT	YES	TIME IMPACT	POSSIBLE
+ P157,000.00 indicative, plus rework to be quantified.		Unit lead time and ceiling rework — assessed in Change Order No. 1	

Please confirm this instruction in writing within **two (2) working days** of receipt. If we receive no written objection within that period, we will proceed on the basis that this confirmation is accurate.

CONFIRMED BY (MRK)

Engr. Mark Raphael Tive

Project Manager · MRK Construction Corporation

SIGNATURE

DATE _____

18 Sep 2026

OWNER'S CONFIRMATION

1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	32	33	34	35	36	37	38	39	40	41	42	43	44	45	46	47	48	49	50	51	52	53	54	55	56	57	58	59	60	61	62	63	64	65	66	67	68	69	70	71	72	73	74	75	76	77	78	79	80	81	82	83	84	85	86	87	88	89	90	91	92	93	94	95	96	97	98	99	100
101	102	103	104	105	106	107	108	109	110	111	112	113	114	115	116	117	118	119	120	121	122	123	124	125	126	127	128	129	130	131	132	133	134	135	136	137	138	139	140	141	142	143	144	145	146	147	148	149	150	151	152	153	154	155	156	157	158	159	160	161	162	163	164	165	166	167	168	169	170	171	172	173	174	175	176	177	178	179	180	181	182	183	184	185	186	187	188	189	190	191	192	193	194	195	196	197	198	199	200
201	202	203	204	205	206	207	208	209	210	211	212	213	214	215	216	217	218	219	220	221	222	223	224	225	226	227	228	229	230	231	232	233	234	235	236	237	238	239	240	241	242	243	244	245	246	247	248	249	250	251	252	253	254	255	256	257	258	259	260	261	262	263	264	265	266	267	268	269	270	271	272	273	274	275	276	277	278	279	280	281	282	283	284	285	286	287	288	289	290	291	292	293	294	295	296	297	298	299	300
301	302	303	304	305	306	307	308	309	310	311	312	313	314	315	316	317	318	319	320	321	322	323	324	325	326	327	328	329	330	331	332	333	334	335	336	337	338	339	340	341	342	343	344	345	346	347	348	349	350	351	352	353	354	355	356	357	358	359	360	361	362	363	364	365	366	367	368	369	370	371	372	373	374	375	376	377	378	379	380	381	382	383	384	385	386	387	388	389	390	391	392	393	394	395	396	397	398	399	400
401	402	403	404	405	406	407	408	409	410	411	412	413	414	415	416	417	418	419	420	421	422	423	424	425	426	427	428	429	430	431	432	433	434	435	436	437	438	439	440	441	442	443	444	445	446	447	448	449	450	451	452	453	454	455	456	457	458	459	460	461	462	463																																					

☐ Confirmed — proceed with Change Order No. 1 ☐ Not confirmed — keep wall-mounted inverter units


NAME / POSITION

SIGNATURE

DATE _____

PROJECT SCHEDULE

PROJECT :	SM ILOILO PUBLIC CENTRAL MARKET
LOCATION :	Iloilo City Proper, Iloilo City
SUBJECT :	PROPOSED OVERALL WORK SCHEDULE
DATE :	46,244.31 sqm (BUA) 29,683.41 sqm (GFA)

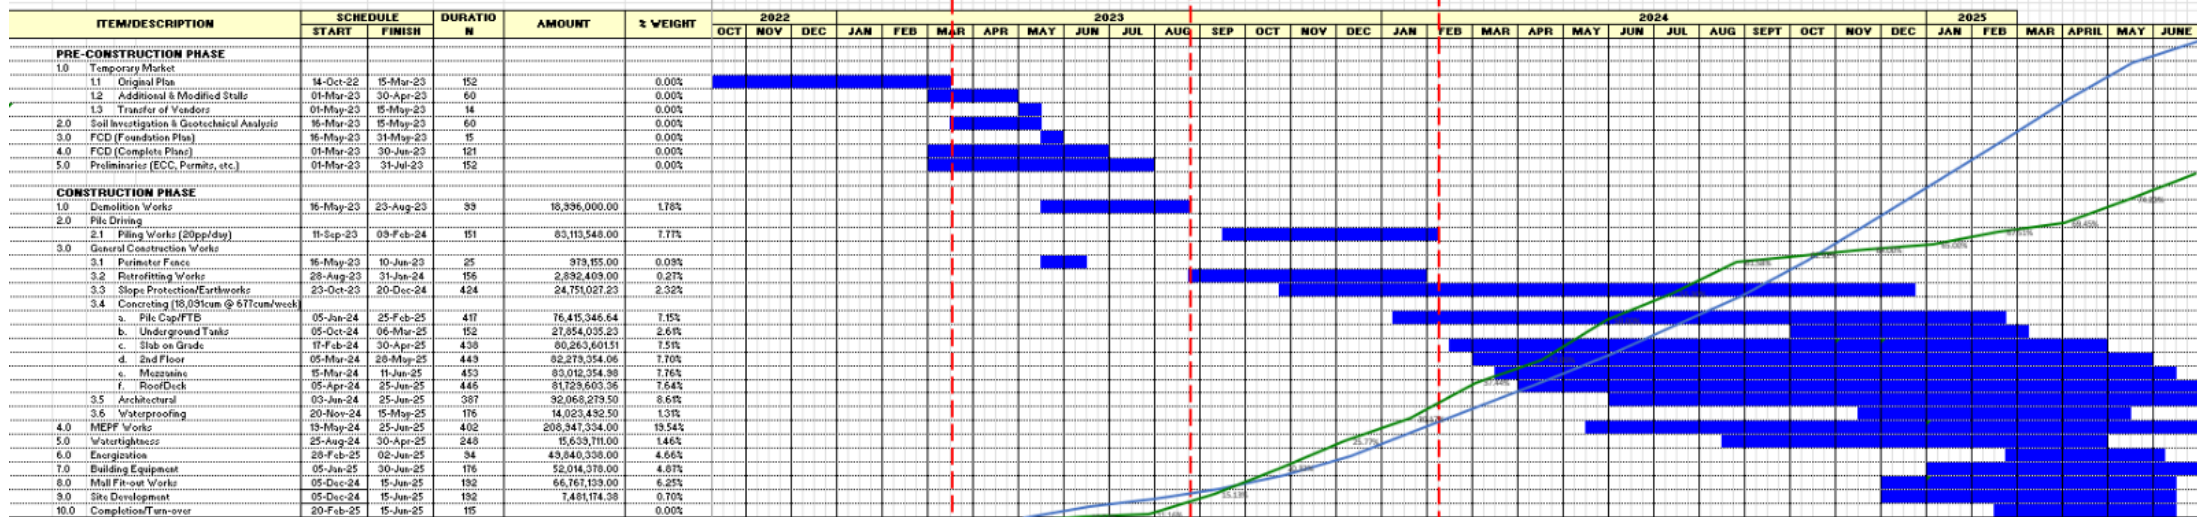

Accomplishment	
Planned	: 97.57%
Actual	: 80.85%
Variance	: -15.62 %

PROJECT SUMMARY


PROJECT TIMELINE	DATE
Construction Start	JULY 29, 2023
Project Completion	AUGUST 30, 2025

PROJECT DURATION	DAYS	%
Construction Duration	763	100%
Days Elapsed	733	96%
Days To Go	30	4%

OVER-ALL STATUS	PREVIOUS REPORT (% Accomplishment)	THIS REPORT (% Accomplishment)	TO-DATE (% Accomplishment)
Plan	96.47%	1.1%	97.57%
Actual	80.85%	1.2%	82.05%
Variance	-15.62%	0.10%	-15.52%
Days delay			75

GROUND FLOOR - CONCRETING

	ACCOMPLISHMENT TO DATE	BALANCE TO COMPLETE	COMPLETION DATE	REMARKS
SOG	92 %	8%	July 25, 2025	Ongoing Preparation Prior To Concreting Works
SITE DEVELOPEMENT	10%	90%	Sept 17, 2025	Ongoing Site Development Works

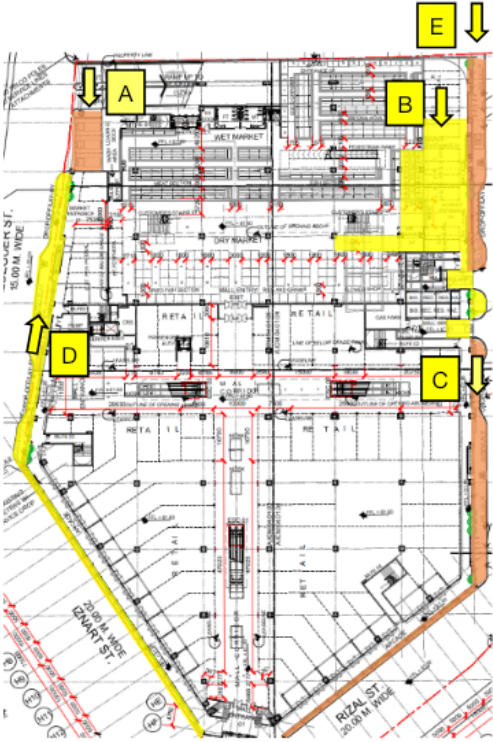

LEGEND		
 DONE	 ONGOING	 BALANCE
